



CONSTRUCTION MANAGEMENT PLAN LIMELIGHT HOTEL

PREPARED FOR THE CITY OF KETCHUM, IDAHO





Equal Opportunity Employer

Table of Contents

A. General Information and Schedule	
a. General Information	Pg. 1
b. Site Location Map	Pg. 2
c. Anticipated Project Schedule	Pg. 3
B. Excavation	
a. Trucking Route	Pg. 4
b. Site Logistics Plan	Pg. 5
C. Vehicle Parking and Traffic Control	
a. Parking Plan	Pg. 6
b. Traffic Control Plan	Pg. 7
D. Material Storage/Deliveries	
a. Storage/Laydown Map	Pg. 8
E. Temporary Restrooms, Job Trailers, Dumpsters.	
a. Temporary Facilities Map	Pg. 9
F. Screening	
a. Fencing Outline	Pg. 10
G. Use of Rights of Way	
H. Noticing	Pg. 11

Project Owner-Limelight Ketchum, LLC

Construction Manager:	Mark Vogele	970.923.8759
Project Manager AIA:	Gert Van Moorsel	970.923.8757
Owner Representative:	Jim Garrison	206.914.1404

McAlvain Project Contacts

Owner:	Torry McAlvain	208.870.9336
President:	Chuck Graves	208.830.5702
Project Director:	Walt McBrier	208.871.1575
Project Manager:	Derek Jensen	208.789.6562
Superintendent:	Brian Murphy	208.871.1576
Project Engineer:	Andrew Bailey	208.908.5994



Equal Opportunity Employer

A. General Information and Schedule

The Limelight Hotel project site is located in Ketchum, Idaho on the west side of State Highway 75, bordered by River Street, Washington Street, and First Street, more fully described as Lot 1A, Block 20, City of Ketchum, Blaine County, Idaho.

The proposed project is a five story hotel, with one story below grade. The program includes a main level for guest drop-off and check-in, guest and public amenity functions including conference rooms, fitness center, lounge and lobby areas, board room, game room, ski and bike storage, a retail store, and outdoor pool and terrace areas. Also on the main level are functions supporting the hotel services including a kitchen, restrooms, administration offices, back of house spaces, and a loading service dock. Levels two through four include 100 hotel rooms. Levels four and five include 14 for sale condominium units with 10 lock-off units. The below grade level program includes approximately 100 parking spaces and back of house functions. The total area of the building is proposed to be approximately 180,000 square feet. This project is seeking LEED Gold Certification.



Equal Opportunity Employer

Anticipated Project Schedule

5/4/15-6/9/15	Idaho Power and Cox Communications River St and Washington Ave. Undergrounding
5/29/15	Permit Submittal
6/1/15	Mobilization (Trailer setup, temporary fencing, traffic control signage)
6/15/15	Excavation Groundbreaking (Pending Permit)
7/15/15	Excavation Complete (Mass Haul trucking complete)
8/1/15	Tower Crane Mobilization
7/15/15	Structural foundations and concrete deck
11/1/15	Site backfill
12/1/15- 11/1/16	Building Envelope Systems and Finishes
11/1/15-12/15/16	Landscaping/Site Furnishings/Final Inspections


B. Excavation

Excavation is proposed to begin June 15th, 2015. Site construction will be conducted from 7:30am to 5 pm, Monday through Saturday. 2 excavators will load the dirt, with a team of 20 dump trucks moving the excess material offsite to Walker Sand and Gravel located at 100 Walker Dr., Bellevue, ID. Other suitable locations will be entertained if made available. Trucks will enter town from the south on Hwy 75. They will enter the site off of First Street. When exiting they will proceed down River St., turn right on HWY 75 heading south. Trucks leaving the site will have beds properly sealed and covered. Truck tires will be clean when exiting the site. Streets will be swept/washed as needed to maintain a clean right of way. Trucks will not idle for longer than 3 minutes. Staging for trucks will be at point of disposal. All site run-off will be contained onsite, and managed according to the SWPPP plan.

**Hours of construction will be
7:30am-7:00pm. Monday-Friday
9:00am-6:00pm Saturday**




Limelight Hotel Site Logistics Plan 4-17-15

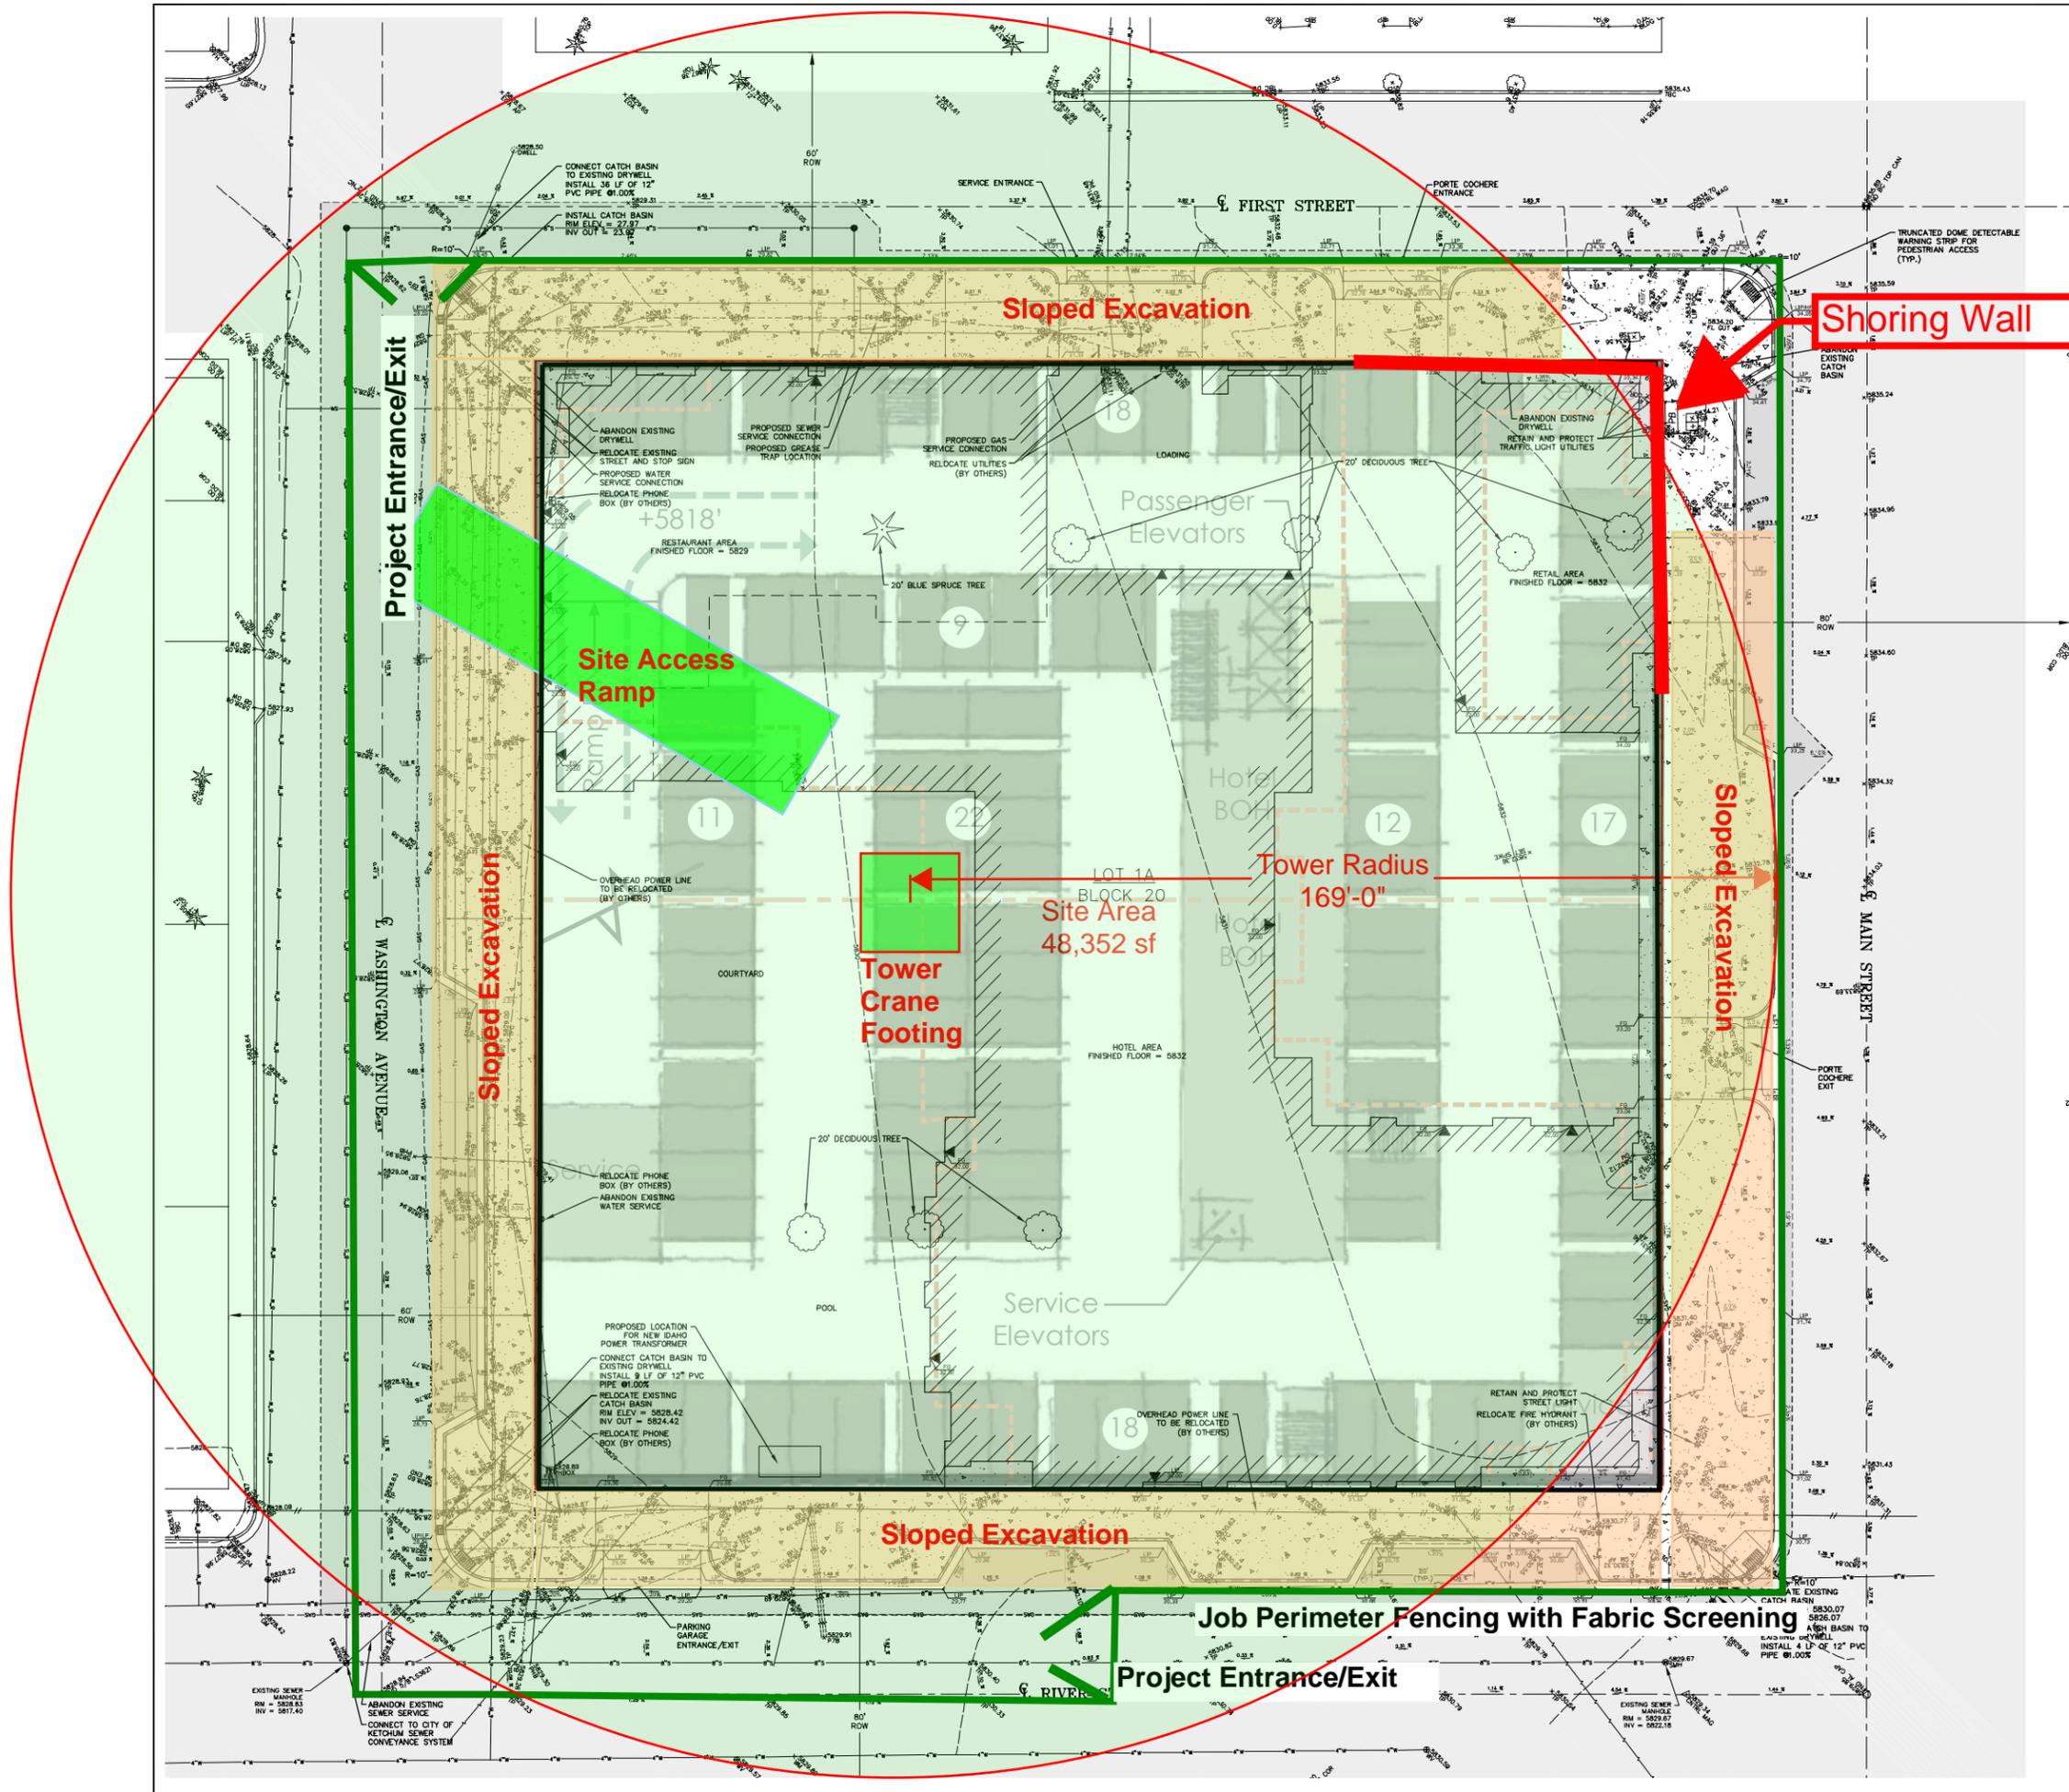


C. Vehicle Parking and Traffic Control

Limited vehicle parking will be conducted in the “Doll House” lot (directly NW across 1st St), and the vacant lot located at 2nd St W and 2nd Ave. (Lots to be leased, pending approval of the CMP). River Run parking lot will be utilized for trade parking, and workers will be shuttled to the site. Traffic control will be conducted per plan. Flaggers will be utilized on an as needed basis when moving equipment and materials.

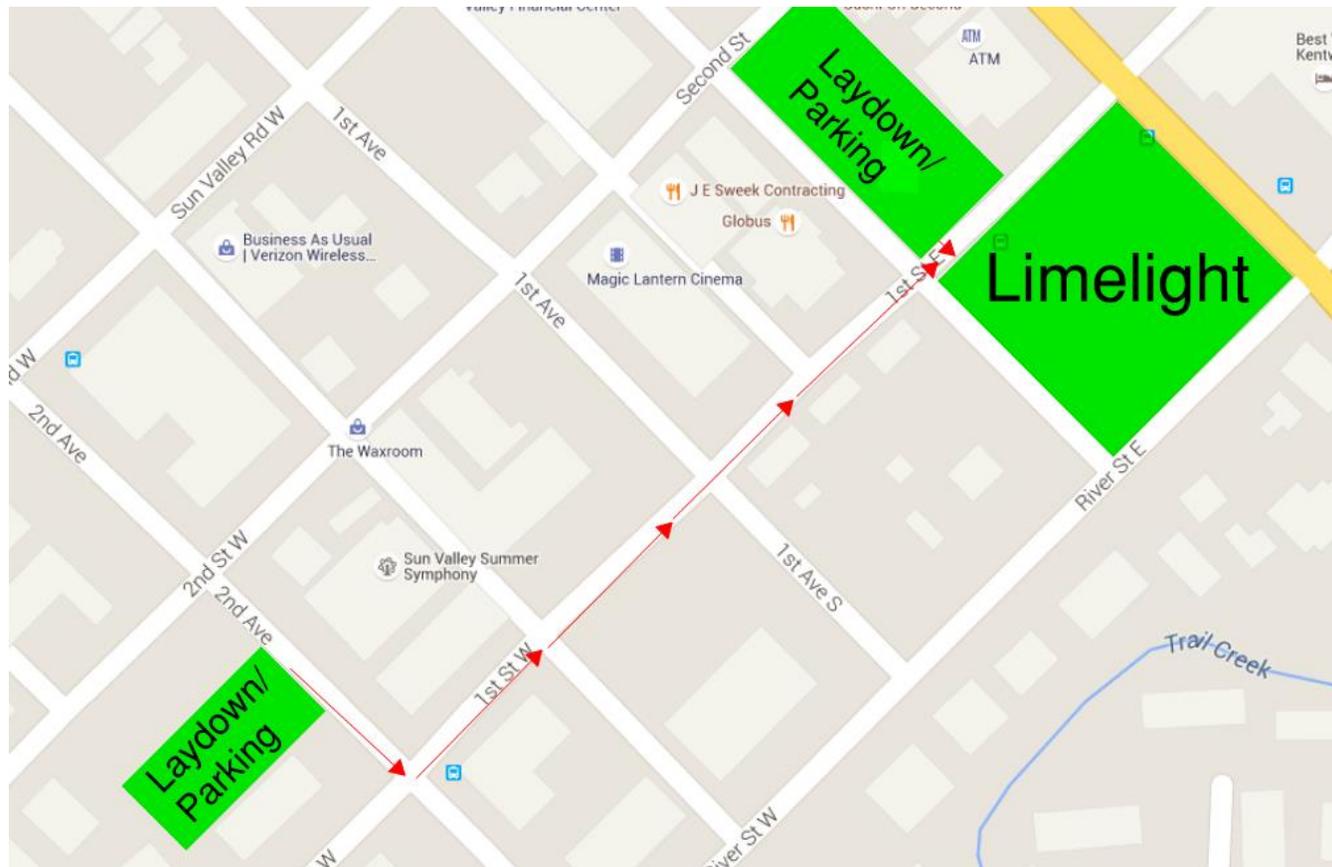

Traffic Control Plan

Concrete pours will be conducted from inside the project gate.
 Material deliveries will be unloaded inside the gate or on the proposed lay down areas, within the gate.
 In special cases where the task at hand must be completed outside the gate, proper noticing, flagging, and traffic control will be scheduled.

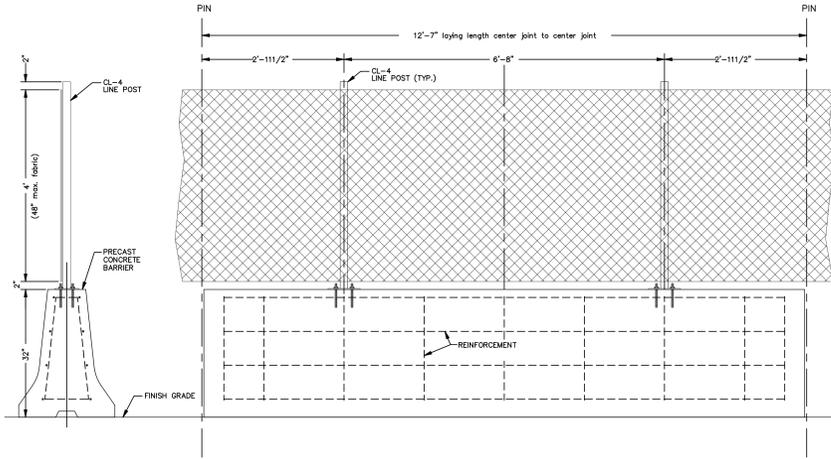

CHAIN LINK FENCE ON CONCRETE BARRIER DETAIL
 NOT TO SCALE


NOTES

1. ALL SIGNS, TRAFFIC CONTROL DEVICES, AND CRASH CUSHIONS SHALL CONFIRM TO THE CURRENT MUTCD. THE CONTRACTOR SHALL PROVIDE AN ADEQUATE NUMBER OF BARRICADES, SIGNS, AND MANPOWER TO PREVENT ALL PUBLIC ACCESS TO THE CONSTRUCTION AREA.
2. THE CONTRACTOR SHALL PROVIDE, ERECT, AND MAINTAIN ALL TRAFFIC CONTROL DEVICES AS REQUIRED BY THESE PROJECT DOCUMENTS, THE KETCHUM STREET DEPARTMENT, LTD, OR THE OWNER TO PROTECT THE PUBLIC DURING ALL STAGES OR THE WORK FOR THE DURATION OF THE PROJECT. THE OVERALL EFFECTIVENESS UNDER BOTH DAY AND NIGHT CONDITIONS AND THE PLACEMENT OF THESE INSTALLATIONS SHALL BE MAINTAINED, AND ADJUSTMENTS AND CLEANING DONE TO ENSURE OPTIMUM PERFORMANCE OF THE TRAFFIC CONTROL DEVICES.
3. THE CONTRACTOR SHALL SUBMIT ANY CHANGES TO THE CONTROL PLAN FOR APPROVAL BY OWNER, LTD, AND THE KETCHUM STREET DEPARTMENT. NO CHANGES TO THE TRAFFIC CONTROL PLAN SHALL BE IMPLEMENTED UNTIL APPROVAL OR CHANGES ARE RECEIVED IN WRITING.
4. THE CONTRACTOR SHALL COVER EXISTING TRAFFIC CONTROL SIGNS IN CONSTRUCTION ZONE.

LEGEND

- TEMPORARY 6' HIGH CHAIN LINK FENCE PANELS
- CONCRETE JERSEY BARRIER W/ CHAIN LINK FENCE ON TOP (SEE DETAIL THIS SHEET)
- PROJECT SITE / WORK AREA

SIGN SUMMARY		
TYPE	DESCRIPTION	QUANTITY
G20-2	CRASH BARREL	6
R4-8	END ROAD WORK	5
R8-3	KEEP LEFT (SYMBOL)	1
R8-3	NO PARKING	1
R9-9	SIDEWALK CLOSED	8
R9-11	SIDEWALK CLOSED AHEAD CROSS HERE	7
W20-1	ROAD WORK AHEAD	7

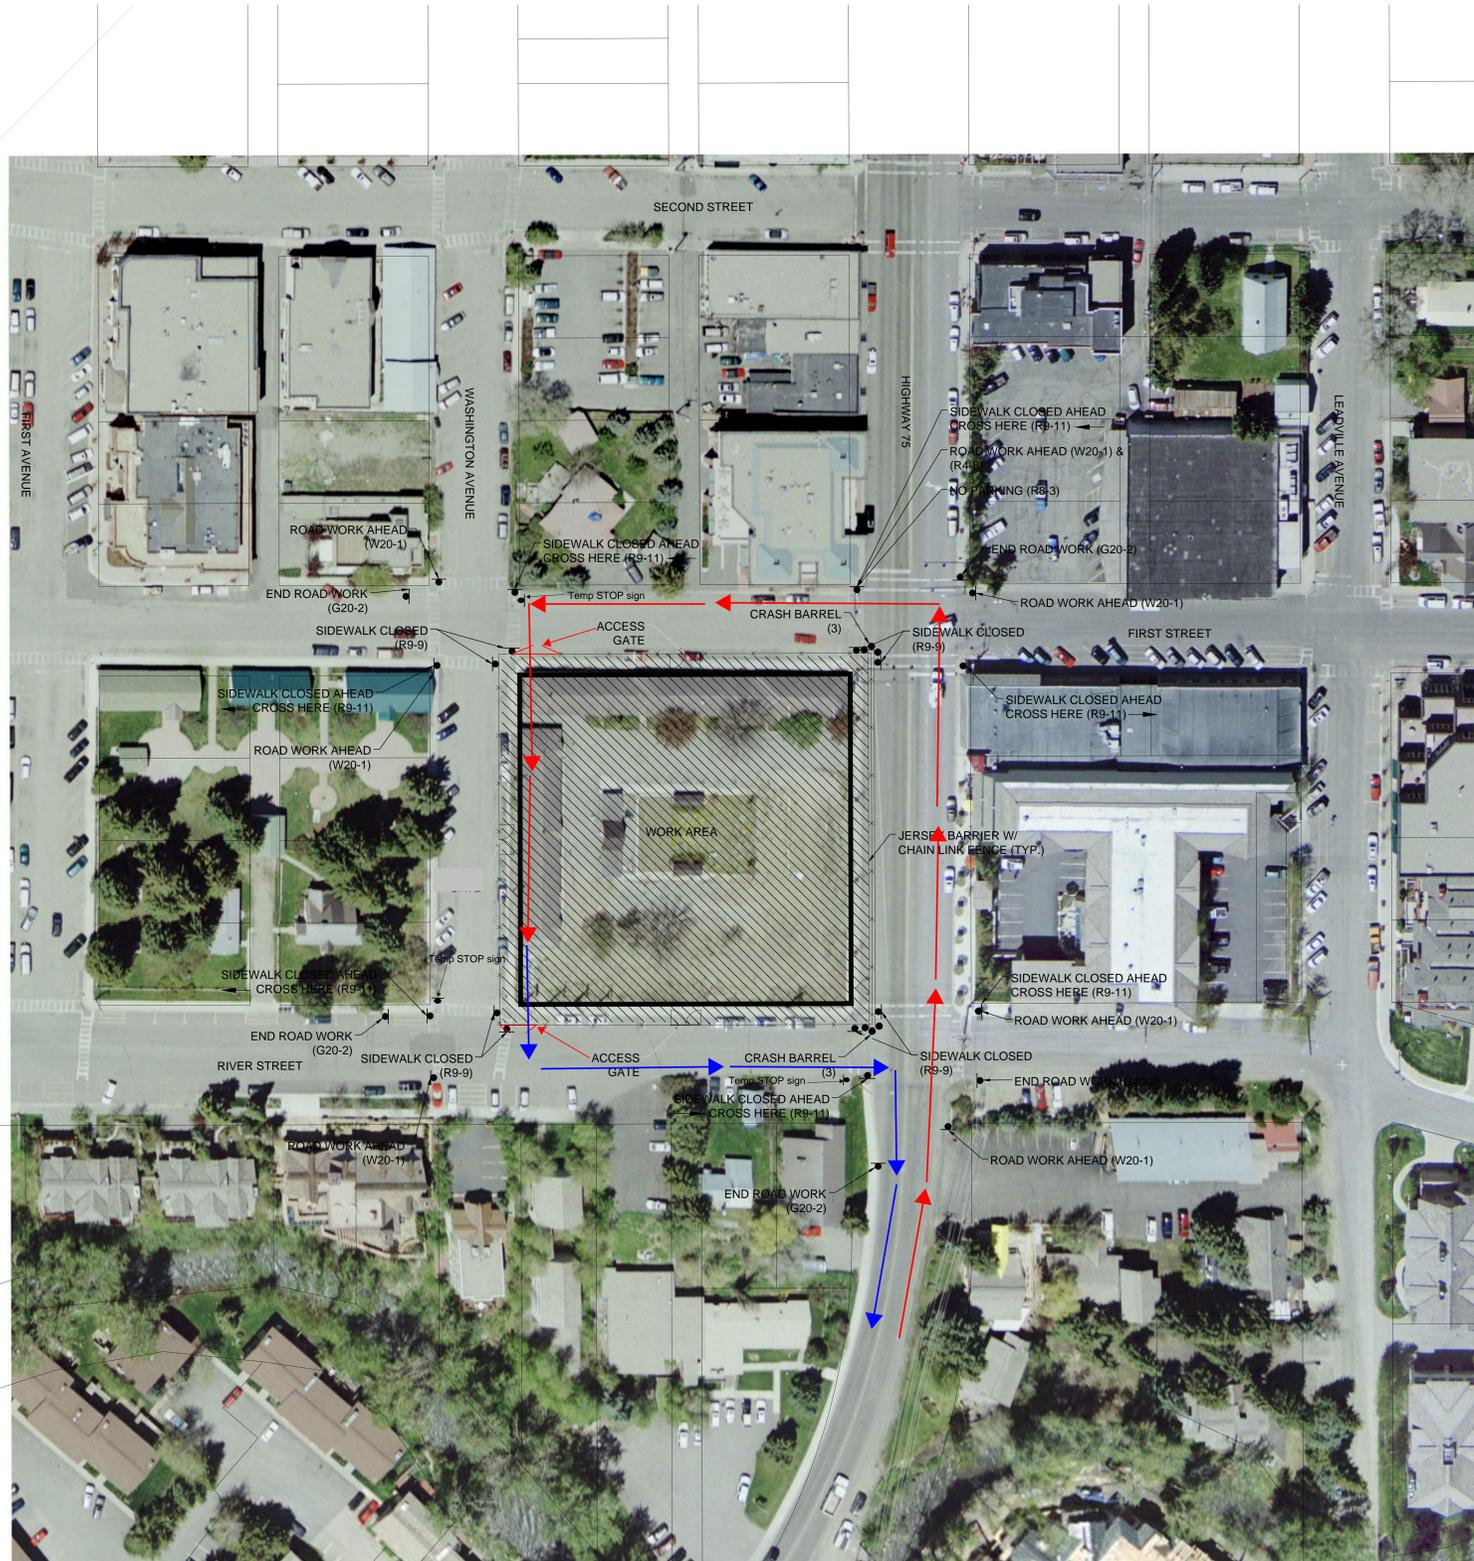

G20-2
END ROAD WORK


R4-8

R8-3

R9-9
SIDEWALK CLOSED

R9-11
SIDEWALK CLOSED AHEAD CROSS HERE

W20-1
ROAD WORK AHEAD



ORIGINAL SIGNED BY JEFF C. LOOMIS
 DATE ORIGINAL SIGNED: 04-09-2015

ORIGINAL ON FILE AT OFFICE OF
 GALENA ENGINEERING (HAILEY, ID)

TRAFFIC CONTROL PLAN
LIMELIGHT HOTEL
 LOCATED WITHIN THE CITY OF KETCHUM, BLAINE COUNTY, IDAHO
 PREPARED FOR ASPEN SHING COMPANY, LLC
 PROJECT LOCATION: P:\Ketchum\5433\5433.dwg
 PROJECT NUMBER: 5433
 DATE: 4/10/2015 8:44:01 AM MDT
 SHEET 1 OF 1
 REVISIONS
 NO. DATE BY
 GALENA ENGINEERING, INC.
 Civil Engineers & Land Surveyors
 317 N. River Street
 Ketchum, ID 83701
 (208) 788-1700
 www.galena-engineering.com


D. Material Storage/Deliveries

Material storage/laydown/delivery areas are highlighted in green, which include the “Doll House” lot, as well as the lot at 2nd St/2nd Ave.(The areas proposed are pending CMP acceptance prior to leasing the properties) Materials/tools/equipment/personnel will enter and exit the jobsite and allocated laydown areas using proper notification, flaggers, and equipment as required.




E. Temporary Restrooms, Job shacks, Dumpsters.

Temporary restrooms and job trailers will be located on the Doll House lot. Dumpsters will be placed on the Washington street existing curb line within the project fencing. See map below.

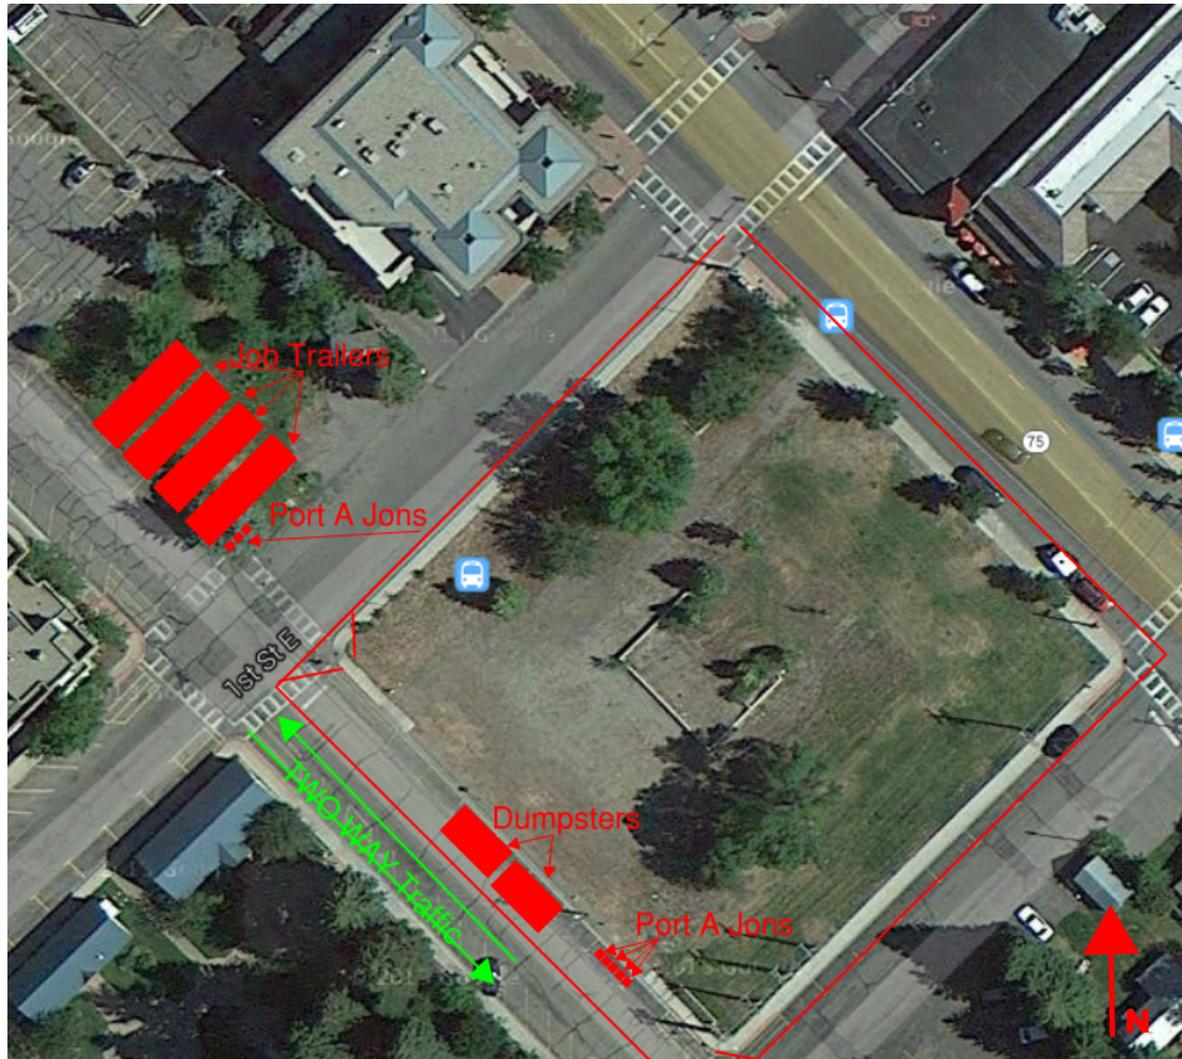

F. Fencing/Screening

Temporary 6' fencing will be screened from top to bottom on 1st St, River St, and Washington Street. A concrete barrier wall, with fencing above will be utilized on Main St. It will be maintained in a clean, orderly and aesthetically pleasing fashion.

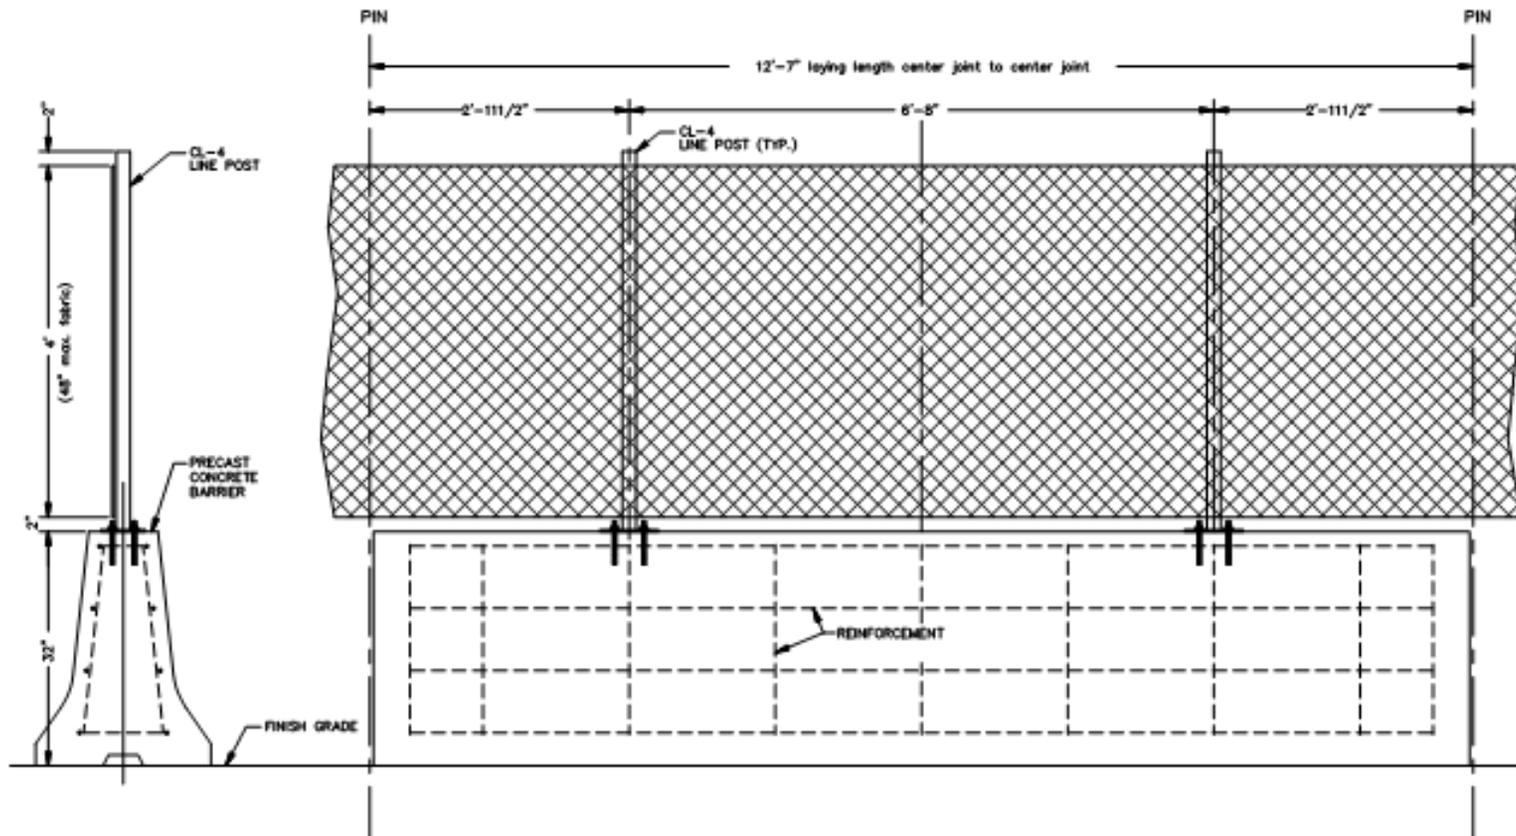

CHAIN LINK FENCE ON CONCRETE BARRIER DETAIL
NOT TO SCALE



Equal Opportunity Employer

G. Use of Rights of Way

Perimeter site parking will be utilized accordingly. 8 Spots on River Street, 20 spots on Washington Avenue (8 spots east side, 12 west side), 7 on First Street, and the parking/taper lane on Main Street.

- **Antique Show- (July 2-5) Two way traffic will be maintained on Washington Avenue.**
- **Ketchum Alive- (Tuesdays 7-9pm June 13th-August) No impact. The jobsite will shut down at 6pm on these days, and provide clear access to these events.**

H. Noticing

Traffic control signs will be installed per plan, notifying pedestrians, and the traveling public of the path of ease. Job signs will be posted on board/fence per City of Ketchum guidelines. City Arborist will be notified prior to any trenching along the west side of Washington Ave to ensure no damage to tree roots. We do not anticipate any trenching at this time. MCI will provide 3 days' notice to the Street Department for street closures. Onsite signage will be provided with MCI contact information for constructive comments.
